



KSC Flight Hardware Quicklook/STS Mainline Facilities


Launch Pad 39B



Launch Pad 39A



MLP-3 Corrosion Control at Pad A
Move to East Parksite 10/15/01



Refurb/Parksite (East)




Refurb/Parksite (West)


Suspect (Railcars)



RPSF Surge 1 (STS-109)



RPSF Surge 2 (STS-108) (STS-110)




KSC(SLF) /DFRC




Roberts Road Site

(STS-110) (STS-111)



RPSF (STS-110) (STS-111)

Rotation/Processing Surge Facility

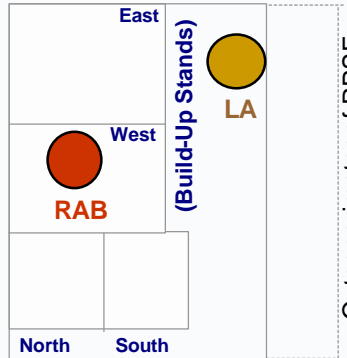

(Inspection Stands)

Orbiter Processing Centers

ROLL TO VAB HB-3: 12/3/01



STS-109 OV-102

Bay 3

Legend (Assignments)


- STS-108/OV-105 Fit HW
ET-111 / MLP-1 / VAB HB1 / PAD A
RSRM 82-SRB BI-110
- STS-109/OV-102 Fit HW
ET-112 / MLP-2 / VAB HB3 / PAD A
RSRM 83-SRB BI-111
- STS-110/OV-104 Fit HW
ET-114 / MLP-3 / VAB HB1 / PAD B
RSRM 85-SRB BI-112
- STS-111/OV-105 Fit HW
ET-113 / MLP-1 / VAB HB3 / PAD A
RSRM 84-SRB BI-113
- STS-107/OV-102 Fit HW
ET-93 LWT / MLP-2 / VAB HB1 / PAD B
RSRM 86-SRB BI-114

- OV-102: Columbia - OPF-3
- OV-103: Discovery - OPF-2
- OV-104: Atlantis - VAB-HB 4
- OV-105: Endeavour - OPF-1

High-Bay 3
MLP-2 to VAB 9/7/01
(NIB to Mod period)


VAB HB-3
Mod Window
Begin: 7/2/01
End: 9/12/01

High-Bay 1
ET Mate: 9/25/01



Start Stack: 8/27/01

OPR:
NASA - J. Angermeier, PH-M1 1-9215
Contact: C. Downs, USA Manifest Plng. 1-7424
31 August 2001



OV-104 /STS-110



Roll to OPF-2
9/14/01

STS-109
OV-102



ET-112



ET-93

STS-107
OV-102



ET-113



ET-111

STS-108
OV-105

ROLL TO VAB HB-1: 10/24/01



Bay 1 STS-108 OV-105

Bay 2 ROLL TO VAB - STORAGE: 9/14/01



STS-118 OV-103

HMF - OMS/RCS Processing Area

OV-102	FRC2	LP05	RP05
OV-103	FRC3	LP01	RP03
OV-104	FRC4	LP03	RP04
OV-105	FRC5	LP04	RP01

- IN TEST CELL (Critical Path Testing)
- INSTALLED IN ORBITER
- IN TEST CELL (Non-Hazardous Work)
- IN STORAGE
- AT OPF AWAITING INSTL'N.
